

division of Facilities Construction and Management

North Capitol Building

Construction Update

- Concrete super structure is complete
- Mechanical, Electrical and Plumbing continues on all levels
- Basement has topping slab and rail installed for Space Saver shelving
- Completion date has shifted by 6 weeks. 01/09/2026





North Plaza

- Parking structure is complete
- Waterproofing is 60% complete and landscaping is underway
- Belvedere is under construction
- East entrance walls are being cast






Central Plaza

- Demolition of the central plaza is complete
- Mass excavation will be complete in two weeks
- Footings for new parking plaza are underway
- Concrete structure is scheduled to complete Mid November






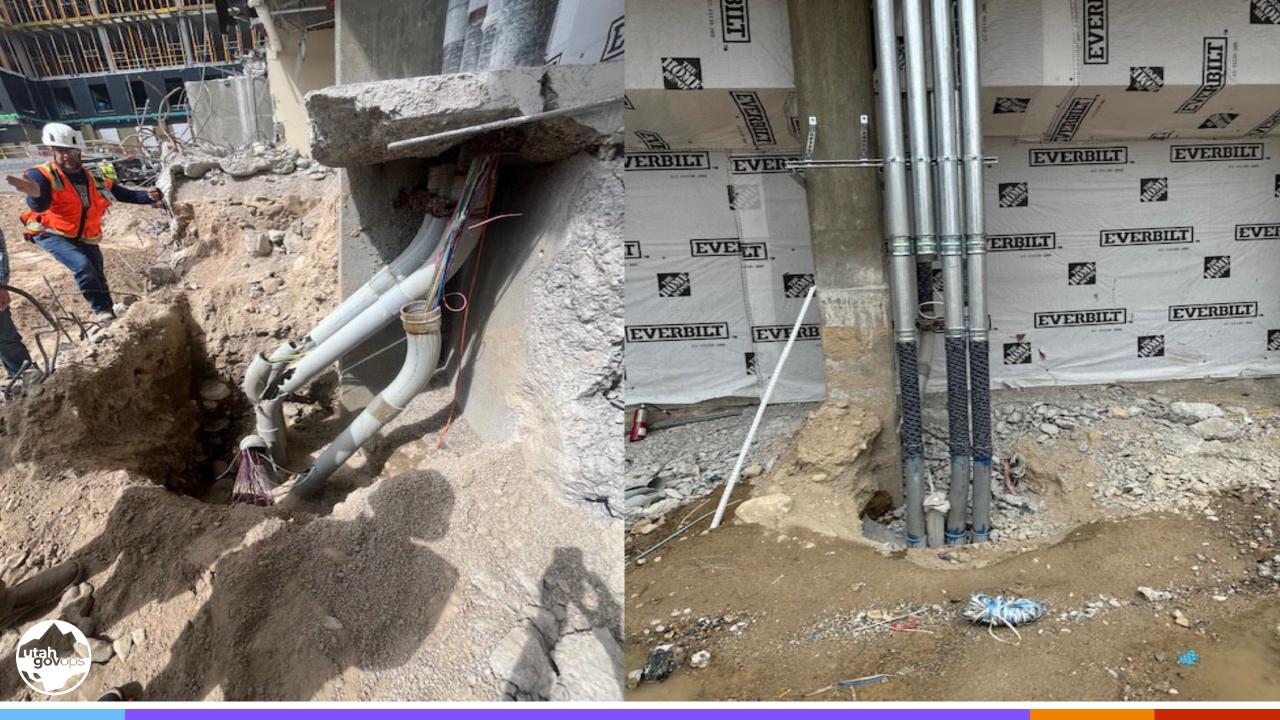







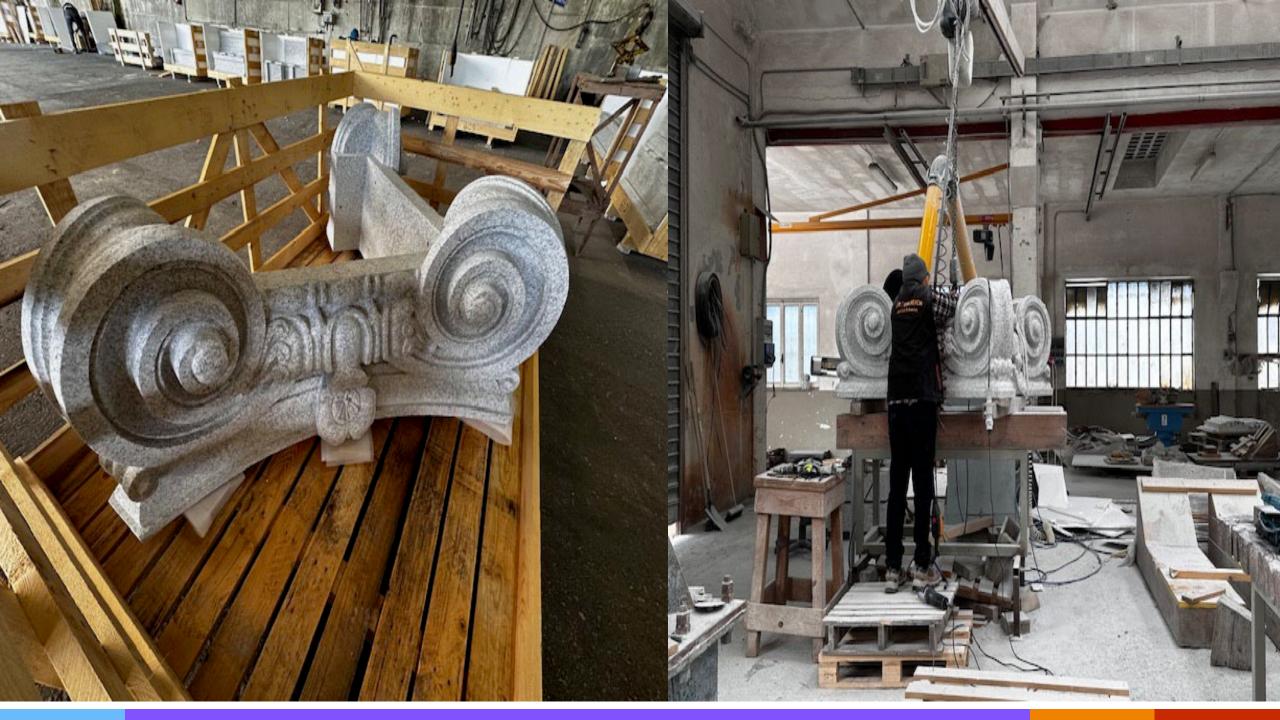

Interior Marble



